DNR 7802.10

TYPE OR USE PEN
SELF TRANSCRIBING
PRESS HARD

WELL LOG AND DRILLING REPORT

Ohio Department of Natural Resources
Divison of Soil and Water Resources, 2045 Morse Road Building B
Columbus, Ohio 43229-6693 Voice (614) 265-6740 Fax (614) 265-6767

1015550

WELL LOCATION

County Preble Township Twin

Owner/Builder (Circle One or Both) Robert (First) Clark (Last)

Address of Well Location 1362 (Number) N. Factory Rd. (Street Name)

City W. Alexandria Zip Code +4 45381

Permit No. 3339 Section/Lot No. (Circle One or Both)

Location of Well in State Plane coordinates, if available: Use of Well Domestic

N ☐ X 39° 43.627 +/- ft. or m

S ☐ Y 84° 31.757 +/- ft. or m

Elevation of Well . +/- ft. or m

Datum Plain: ☐ NAD27 ☐ NAD83 Elevation Source

Source of Coordinates: ☑ GPS ☐ Survey ☐ Other

Sketch a map showing distance well lies from numbered state highways, street intersections, county roads, buildings or other notable landmarks. If latitude and longitude are available please include here: Lat: Long:

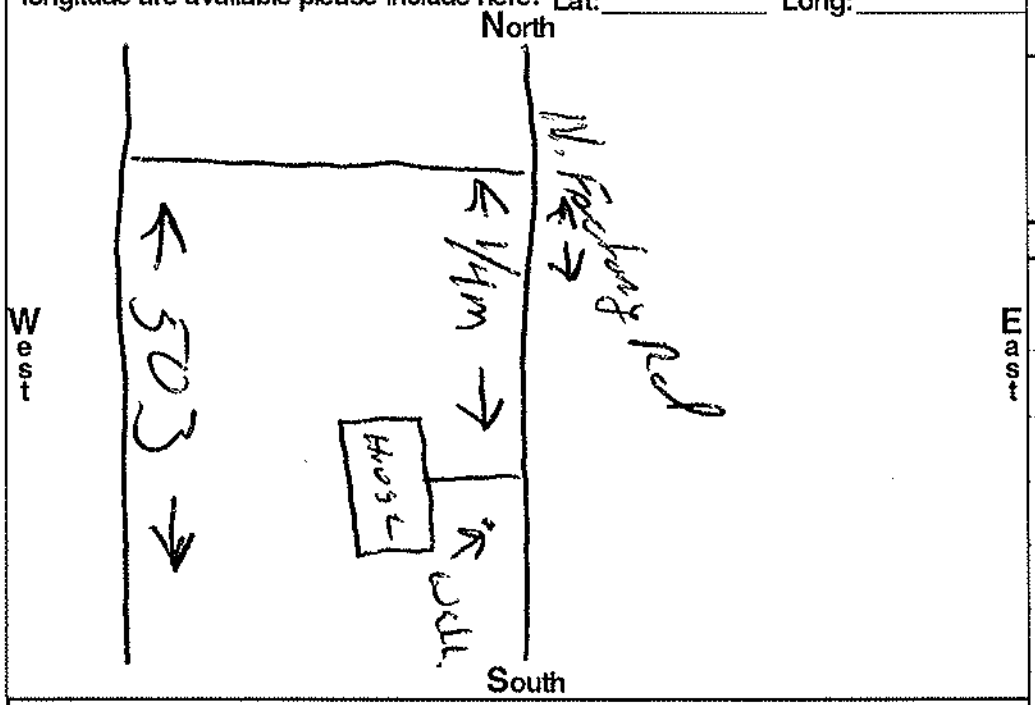

WELL TEST*

Pre-Pumping Static Level 23 ft. Date July 10, 2013

Measured from: ☑ Top of Casing ☐ Ground Level ☐ Other

☐ Air ☑ Bailing ☐ Pumping* ☐ Other

Test Rate 10+ gpm Duration of Test 1 hrs.

Feet of Drawdown -0- ft. Sustainable Yield 10+ gpm

*(Attach a copy of the pumping test record, per section 1521.05, ORC)

Is Copy Attached? ☐ Yes ☐ No Flowing Well? ☐ Yes ☑ No

Quality

PUMP/PITLESS

Type of pump Capacity gpm

Pump set at ft. Pitless Type

Pump installed by

I hereby certify the information given is accurate and correct to the best of my knowledge.

Drilling Firm Wilson Well Drilling & Exc.

Address 155 Beechwood Ave.

City, State, Zip W. Elkton OH. 45070

Signed [signature] Date Feb 15, 14

ODH Registration Number 516

CONSTRUCTION DETAILS

☐ Rotary ☑ Cable ☐ Augered ☐ Driven ☐ Other

BOREHOLE/CASING (measured from ground surface)

1☐ Borehole Diameter 6 inches Depth 49 ft.

Casing Diameter 6 5/8 in. Length 45 ft. Thickness .188 in.

2☐ Borehole Diameter inches Depth ft.

Casing Diameter in. Length ft. Thickness in.

Casing Height Above Ground 18" ft.

Type: 1☐ 2☐ Steel; 1☑ 2☐ Galv.; 1☐ 2☐ PVC; 1☐ 2☐ Other

Joints: 1☐ 2☐ Threaded; 1☑ 2☐ Welded; 1☐ 2☐ Solvent; 1☐ 2☐ Other

SCREEN

Diameter 4 Slot Size .020 Screen Length 5 ft.

Type ~~PVC~~ PVC Material PVC

Set Between 44 ft. and 49 ft.

GRAVEL PACK (Filter Pack)

Material/Size Volume/Weight Used

Method of Installation

Depth: Placed FROM ft. TO ft.

GROUT

Material Benseal Volume/Weight Used 1 bag

Method of Installation dry pour

Depth: Placed FROM 0 ft. TO 49 ft.

DRILLING LOG*

INDICATE DEPTH(S) AT WHICH WATER IS ENCOUNTERED. Show color, texture, hardness, and formation: sandstone, shale, limestone, gravel, clay, sand, etc.	From	To
Brown Clay	0	8
fine Gravel /w sand	8	11
Gray Clay	11	26
Sand	26	42
Sand	42	49

*(If more space is needed to complete drilling log, use next consecutively numbered form.)

Date of Well Completion July 10, 2013 Total Depth of Well 49 ft.

Completion of this form is required by section 1521.05, Ohio Revised Code - file within 30 days after completion of drilling.

ORIGINAL COPY TO - ODNR, DIVISION OF SOIL AND WATER RESOURCES, 2045 MORSE ROAD BLD. B, COLS., OHIO 43229-6693

Blue - Customer's copy Pink - Driller's copy Green - Local Health Dept. copy
