DNR 7802.05e

WELL LOG AND DRILLING REPORT

Ohio Department of Natural Resources
Division of Geological Survey, 2045 Morse Road, Columbus, Ohio 43229-6605
Phone (614) 265-6576

Well Log Number: 3031611

Page 1 of 2 for this record.

WELL LOCATION

County COSHOCTON Township CRAWFORD

JEREMY YODER
Owner/Builder

31122 TR 11
Address of Well Location

City FRESNO Zip Code +4 43824

Permit No. 2026-025 Section; 15 *and or* Lot No.

Use of Well DOMESTIC

Coordinates of Well (Use only one of the below coordinate systems)

Latitude, Longitude Coordinates

Latitude: 40.40403 Longitude: -81.79456

Elevation of Well in feet: 996.1 +/- ft.

Datum Plane: ☐ NAD27 ☐ NAD83 Elevation Source DIGITAL MAP

Source of Coordinates: GPS

Well location written description:

Property is located .52 miles northeast of TR 224, southeast side of TR 11.

Comments on water quality/quantity and well construction:

WELL TEST *

Pre-Pumping Static Level 79 ft. Date 6/10/2026

Measured from GROUND LEVEL

Pumping test method AIR

Test Rate 12 gpm Duration of Test 0.5 hrs.

Feet of Drawdown 0 ft. Sustainable Yield 12 gpm

*(Attach a copy of the pumping test record, per section 1521.05, ORC)

Is Copy Attached? ☐ Yes ☒ No Flowing Well? ☐ Yes ☒ No

PUMP/PITLESS

Type of pump SUBMERSIBLE Capacity 10 gpm

Pump set at 128 ft. Pitless Type AQUA SEAL

Pump installed by FLINNER DRILLING INC.

I hereby certify the information given is accurate and correct to the best of my knowledge.

Drilling Firm FLINNER DRILLING INC

Address 2031 MILLERSBURG ROAD

City, State, Zip WOOSTER OH 44691

Signed ED FLINNER Date 7/22/2026
(Filed Electronically)

ODH Registration Number 00120 Last Revised on 7/22/2026

CONSTRUCTION DETAILS

Drilling Method: AIR ROTARY

BOREHOLE/CASING (Measured from ground surface)

1 Borehole Diameter 9 inches Depth 85 ft.
Casing Diameter 5 in. Length 86 ft. Thickness 0.265 in.

2 Borehole Diameter 5 inches Depth 138 ft.
Casing Diameter in. Length ft. Thickness in.

Casing Height Above Ground 1 ft.

Type 1: PVC
Type 2:

Joints 1: O-RING
Joints 2:

SCREEN

Diameter in. Slot Size in. Screen Length ft.

Type Material

Set Between ft. and ft.

GRAVEL PACK (Filter Pack)

Material/Size Vol/Wt. Used

Method of Installation

Depth: Placed From: ft. To: ft.

GROUT

Material BENTONITE SLURRY Vol/Wt. Used 330 GAL / 750 LBS

Method of Installation PUMPED WITH TREMIE PIPE

Depth: Placed From: 0 ft. To: 85 ft.

DRILLING LOG*

FORMATIONS INCLUDE DEPTH(S) AT WHICH WATER IS ENCOUNTERED.

Color	Texture	Formation	From	To
BROWN		CLAY & SHALE	0	4
BROWN-GRAY		SANDSTONE	4	33
GRAY		SHALE	33	41
GRAY	SANDY	SHALE & SANDSTONE	41	130
GRAY		SHALE	130	138
		WATER AT	90	130

Aquifer Type (Formation producing the most water.) SHALE

Date of Well Completion 07/21/2026 Total Depth of Well 138 ft.

Completion of this form is required by section 1521.05, Ohio Revised Code - file within 30 days after completion of drilling.
Distribute copies of this record to Customer, and Local Health Deptartment.

DNR 7802.05e

WELL LOG AND DRILLING REPORT

Ohio Department of Natural Resources
Division of Water, 2045 Morse Road, Columbus, Ohio 43229-6605
Voice (614) 265-6740 Fax (614) 265-6767

Well Log Number
3031611

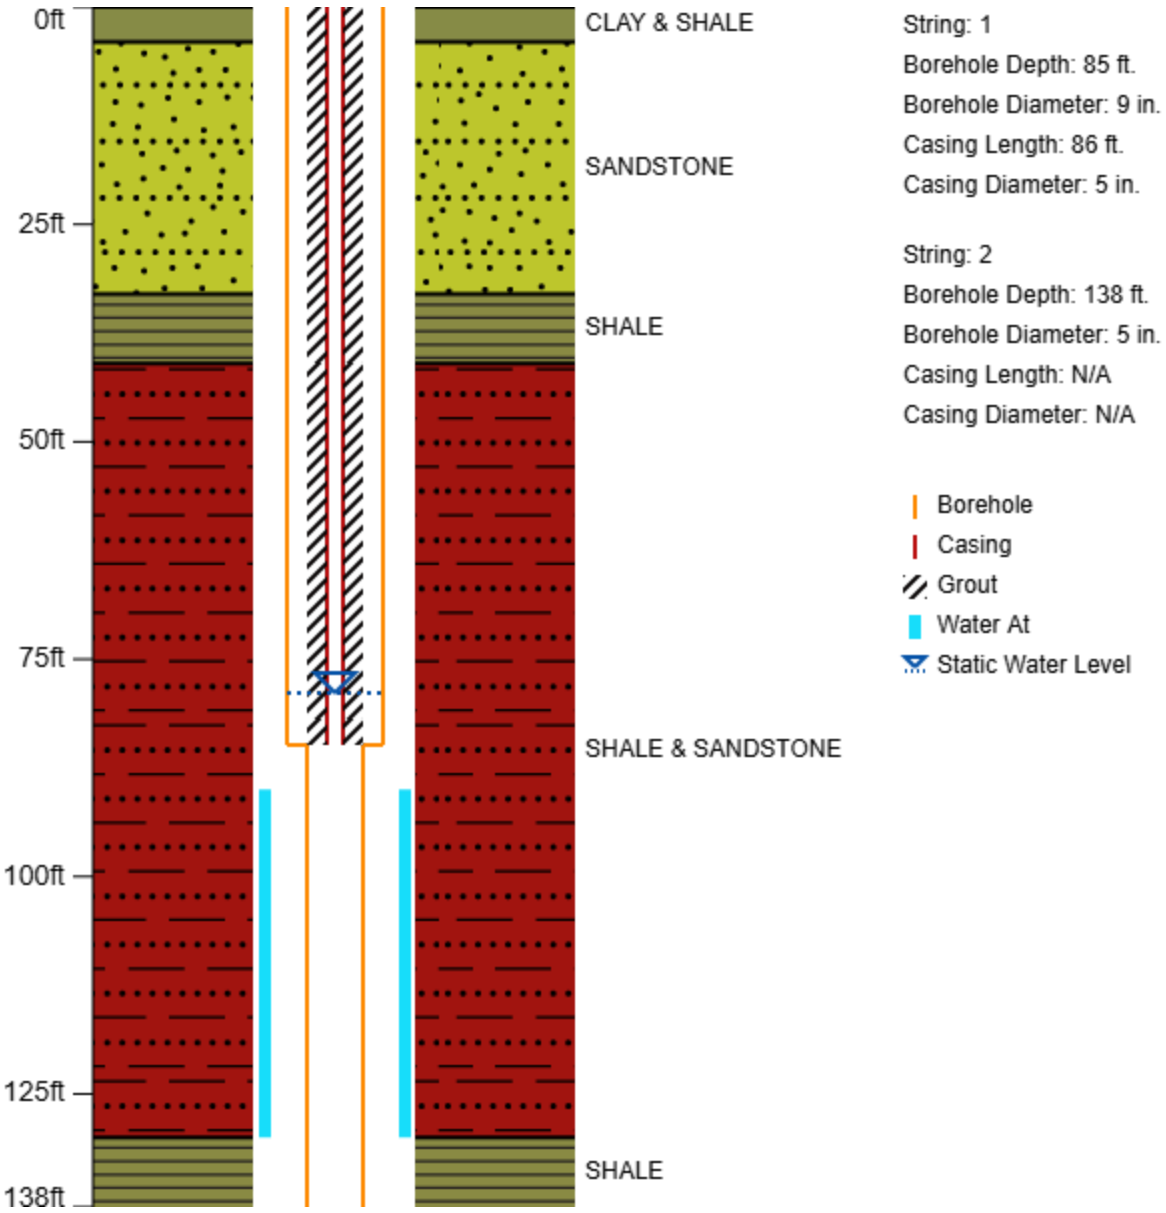

Completion of this form is required by section 1521.05, Ohio Revised Code - file within 30 days after completion of drilling.
Distribute copies of this record to Customer, and Local Health Deptartment.
